



CompTIA

Exam Questions PK0-005

CompTIA Project+ Certification Exam

NEW QUESTION 1

Which of the following is an activity that should be used in the closing phase of a project to support the project triple constraint?

- A. Evaluating the project
- B. Releasing the resources
- C. Closing the contracts
- D. Reconciling the budget

Answer: A

NEW QUESTION 2

A project manager realizes that a project will not be completed on time due to resource constraints. Which of the following actions should the project manager take NEXT?

- A. Trigger the contingency plan and communicate with the stakeholders.
- B. Work with the functional managers to create a work-around.
- C. Submit a change request to the change control board.
- D. Transfer the risk by hiring a new vendor who was successful on a previous project.
- E. Set up an escalation meeting with the sponsor.

Answer: A

NEW QUESTION 3

A PM has identified all the resources involved in a project. The next step is to identify which resources are responsible for which tasks. Which of the following should be used to document this information?

- A. RFI
- B. RACI
- C. WBS
- D. SOW

Answer: B

NEW QUESTION 4

During a staff meeting, a project manager voices a concern about the client billing rate for a particular engineer. Which of the following documents would the project manager need in order to find this information?

- A. SLA
- B. TOR
- C. SOW
- D. NDA

Answer: AB

NEW QUESTION 5

Which of the following should occur when implementing an IT infrastructure change that takes risks into consideration?

- A. Approving the change request
- B. Developing a rollback plan
- C. Gathering necessary resources
- D. Defining requirements

Answer: B

NEW QUESTION 6

During the stabilization phase for recently deployed software, an end user reports a bug that is compromising data integrity. Which of the following tools will the project manager MOST likely use?

- A. Issue log
- B. Defect log
- C. Change log
- D. Task board

Answer: B

NEW QUESTION 7

Due to budgetary and time constraints, a PM scheduled a meeting with all stakeholders during the planning phase to review the requirements and come to an agreement on the minimum viable product that would be acceptable. Which of the following would be used to document this input?

- A. Project change management plan
- B. Project management plan Most Voted
- C. Project transition plan
- D. Project communication plan

Answer:

B

NEW QUESTION 8

A project manager was not part of a contract negotiation. The project manager is concerned that stakeholders will expect the project to achieve deliverables requested in the RFP. Which of the following documents should the project manager produce FIRST to start communication about the boundaries of the project?

- A. Milestone chart
- B. Work breakdown structure
- C. Project charter
- D. Detailed scope statement

Answer: C

NEW QUESTION 9

A third party needs to perform a short-term task for which the duration cannot be accurately estimated and the cost cannot be calculated in advance. Which of the following should the project manager put in place before work begins?

- A. Time and materials contract
- B. Master service agreement
- C. Fixed-price contract
- D. Statement of work
- E. Cost-plus agreement

Answer: A

NEW QUESTION 10

A project manager has been assigned to a new project. During the planning phase, the project manager needs to get an understanding of the purpose of the project. Which of the following should the project manager do?

- A. Collate the lessons learned.
- B. Perform a gap analysis.
- C. Review existing artifacts.
- D. Conduct a retrospective.

Answer: C



NEW QUESTION 10


As a result of an approved change, the project manager updates the project plan with the newest project end date. Which of the following change control processes should the project manager complete NEXT?

- A. Document the request in the change control log.
- B. Communicate the change deployment.
- C. Conduct an impact assessment.
- D. Implement the change.

Answer: C

Explanation:

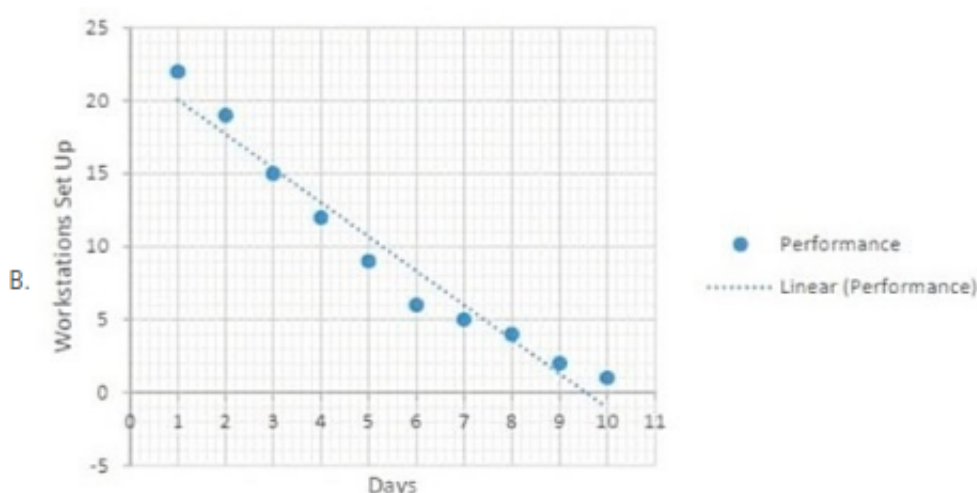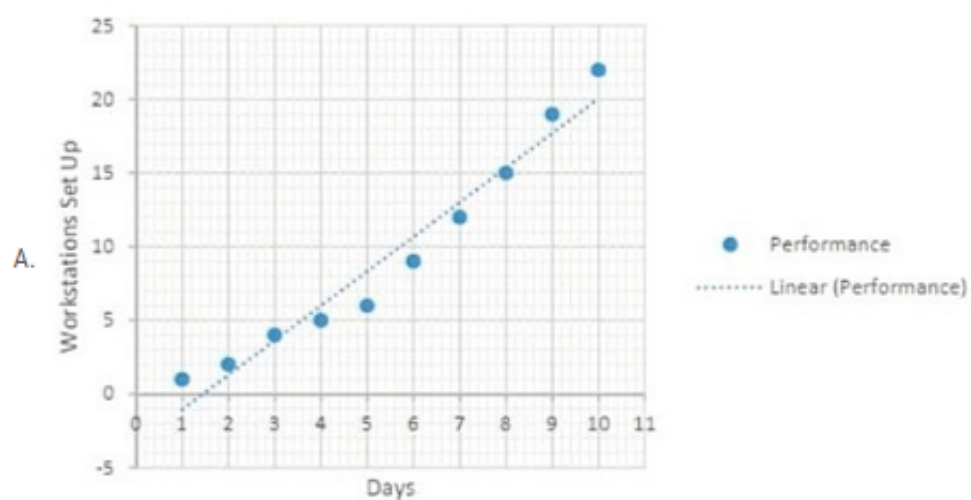

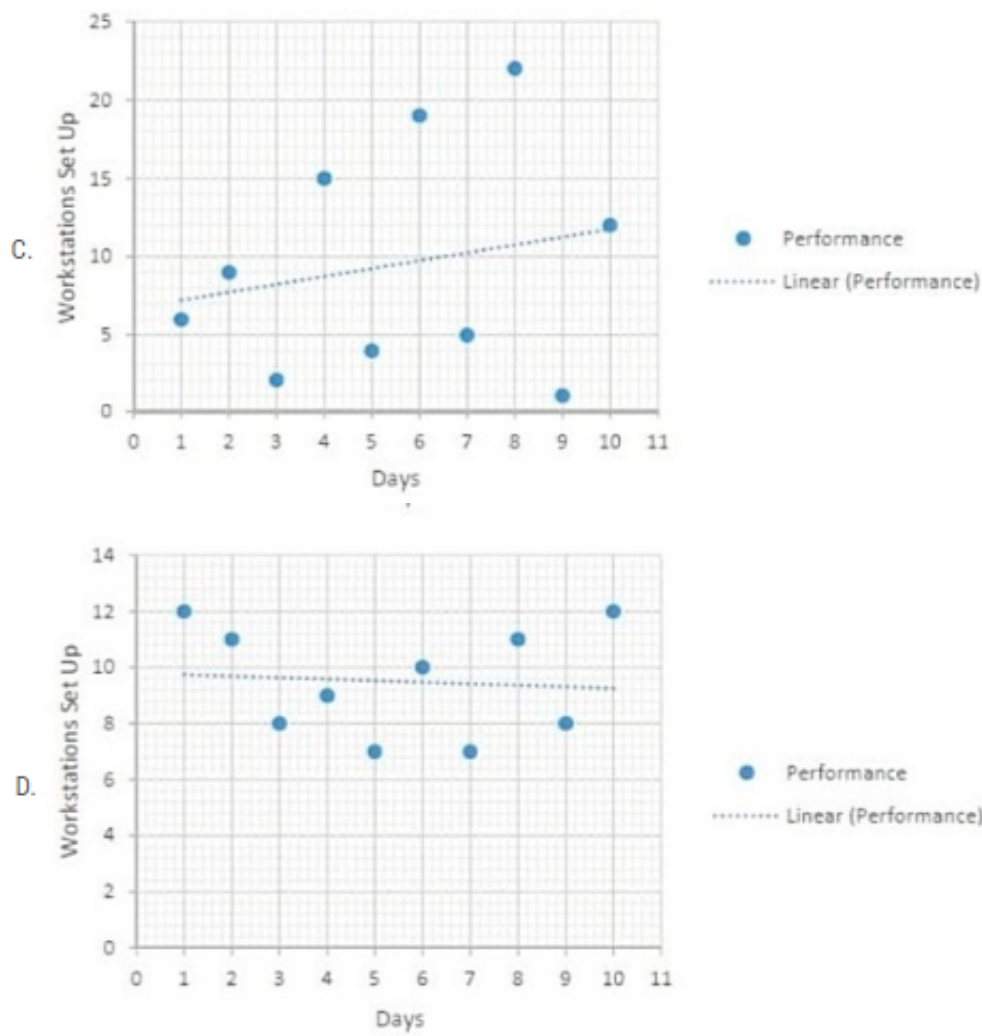

NEW QUESTION 12

Halfway through a project, the sponsor states that the project is taking too long to complete. Which of the following should the project manager consult?

- A. Gantt chart
- B. Maintenance window schedule
- C. Functional requirements
- D. Test results

Answer: A

NEW QUESTION 14


A project manager is assigned to a multinational project with team members from different continents. Which of the following is the MOST important aspect for the project manager to consider?

- A. Resource allocation
- B. Communication security
- C. Technological factors
- D. Cultural differences

Answer: D

NEW QUESTION 18

During a brainstorming session, a project team is elaborating on what caused the unexpected crash of the website that the team was developing. Given the following:

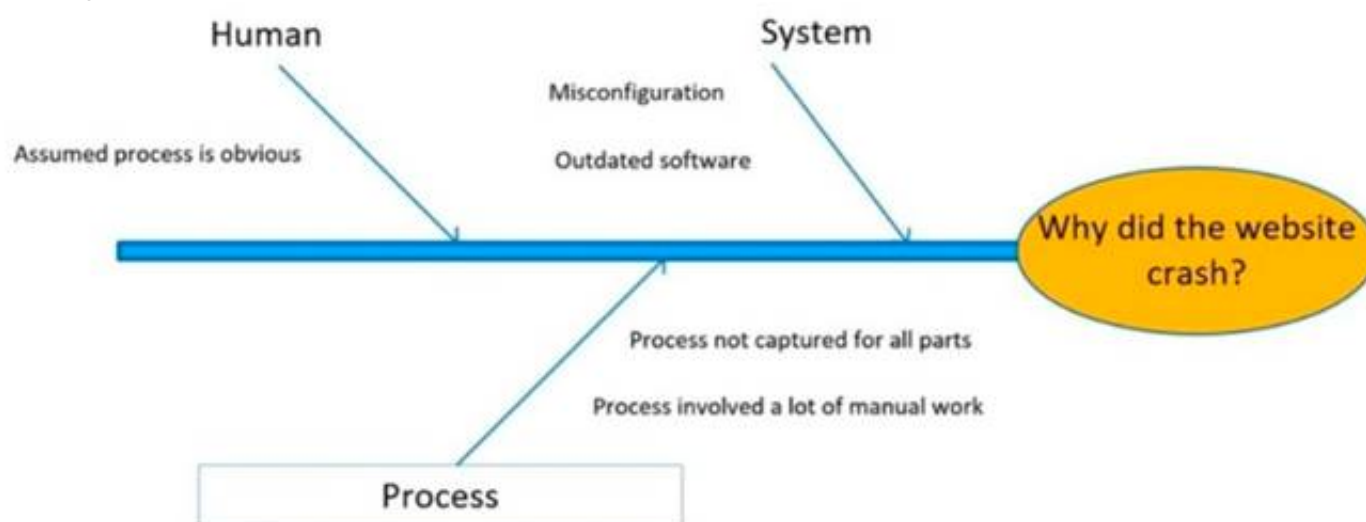

Which of the following was the initial cause of the issue?

- A. Inadequate memory
- B. Incorrect configuration
- C. Lack of infrastructure
- D. Inadequate instructions

Answer: B

NEW QUESTION 19

Which of the following describes three-tier architecture?

- A. Conceptual, design, and implementation stages
- B. Presentation, application, and data processing
- C. Network, software, and security
- D. Development, testing, and production environment

Answer: B

NEW QUESTION 22

After determining the appropriate maintenance window, which of the following should occur NEXT in the operational infrastructure change process?

- A. Implement the change.
- B. Approve the test plan.
- C. Notify customers.
- D. Develop a rollback plan.

Answer: B

NEW QUESTION 26

Which of the following items must be protected as PII? (Choose two.)

- A. Job title
- B. Home address
- C. Work phone number
- D. Time zone
- E. Date of birth
- F. Blood type

Answer: BE

NEW QUESTION 28

.....

Thank You for Trying Our Product

We offer two products:

1st - We have Practice Tests Software with Actual Exam Questions

2nd - Questions and Answers in PDF Format

PK0-005 Practice Exam Features:

- * PK0-005 Questions and Answers Updated Frequently
- * PK0-005 Practice Questions Verified by Expert Senior Certified Staff
- * PK0-005 Most Realistic Questions that Guarantee you a Pass on Your FirstTry
- * PK0-005 Practice Test Questions in Multiple Choice Formats and Updatesfor 1 Year

100% Actual & Verified — Instant Download, Please Click
[Order The PK0-005 Practice Test Here](#)
